

Task Management Report

Executive Summary

This report reviews : 15 Projects , 189 tasks, and 30 team members. The overall picture is less than half of planned work is complete, the majority of tasks are past their due date, and over half of assigned staff are stretched across more work than their time allows. None of these issues require new tools to see they are visible today in the existing project data and need management attention this quarter.


The three headline risks are: execution has stalled, with 47% of projects on hold and only one project fully completed, task delivery is significantly behind schedule, with 80% of open tasks past their due date, and key staff are over allocated across multiple concurrent projects, which is both a delivery risk and a retention risk.

Key Measures


Tasks 189 Total tasks	Projects 15 Total projects	Task completion 19.05% 36 tasks marked Done	Overdue tasks 153 Requires recovery plan
On-time delivery 44.44% 16 of 36 completed tasks	48.73% Average project completion	Budget variance 32.90% Positive aggregate variance	Milestones delayed 19 Of 65 milestones

Data includes 4 projects in progress, 7 on hold, 2 cancelled, 1 completed, and 1 in planning. Only one project is fully completed, while 7 projects are currently on hold. Two projects are over budget and three projects show a date based delay.

The aggregate budget is 24.50M compared with 16.44M in actual cost, leaving 8.06M unspent this positive total should not hide project level overruns or stalled delivery.

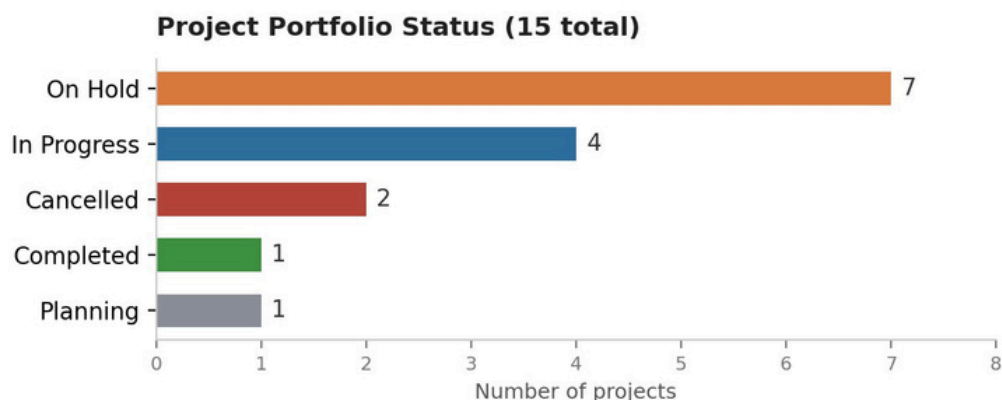

Of 189 tasks tracked, only 36 (19%) are marked Done. 43 tasks (23%) are Blocked, and measured against the most recent activity date in the data 152 tasks (80%) are past their due date.

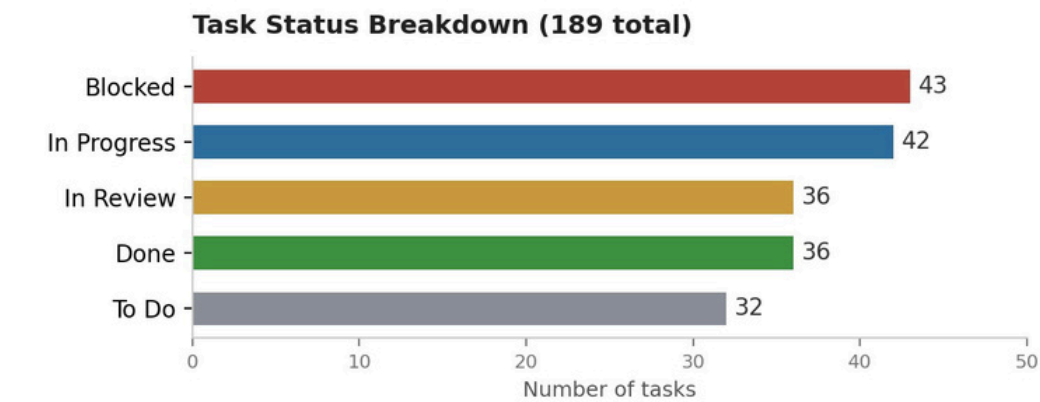

Recommendations

- Overdue work is not concentrated in low priority items: 36 of the 46 Critical priority tasks (78%) are overdue. This means the most important work is being delayed at the same rate as everything else, rather than being protected.
- The team consists of 30 employees (25 active) across 8 departments, the largest being Engineering (6) and QA (5).
- Average performance score across the last review cycle is 3.66 out of 5, and 16 of 60 reviews (27%) recommended a promotion.
- The more urgent finding is workload distribution: of the 25 actively assigned employees, 14 (56%) are allocated above 100% of their capacity across concurrent active projects.
- Explore *the on hold projects now* Seven of 15 projects (47%) are on hold while still carrying committed budget.

Conclusion

The project has a usable management foundation and a positive overall budget position, but execution risk is elevated. The most important leadership decision is to move from reporting activity to managing recovery: unblock work, challenge prolonged on hold projects, protect delivery dates, and rebalance employee capacity.
